

**RISK MANAGEMENT STUDY IN CONSTRUCTION
INDUSTRY IN YOGYAKARTA**

Final Project Report

As one of the requirements to obtain a bachelor's degree from
University of Atma Jaya Yogyakarta



By:

KELVIN FINSEN

Student ID: 16 03 16354

INTERNATIONAL CIVIL ENGINEERING PROGRAM

FACULTY OF ENGINEERING

UNIVERSITY OF ATMA JAYA YOGYAKARTA

APRIL 2020

STATEMENT

I, the undersigned, declare truly that the Final Project is under the title

RISK MANAGEMENT STUDY IN CONSTRUCTION INDUSTRY IN YOGYAKARTA

It's really my own work and not the result of plagiarism from other people's work. Ideas, research data, direct and indirect quotations from other people's writings or ideas are stated in writing in this Final Project. If it is proven later that this Final Project is the result of plagiarism, then the certificate I obtained was declared null and void and I will return it to the Chancellor of University of Atma Jaya Yogyakarta.

Yogyakarta, April 2020

The one who make the statement,

A 10000 Rupiah Indonesian postage stamp is shown with a signature over it. The stamp features the Garuda Pancasila emblem and the text 'REPUBLIK INDONESIA', '10000', and 'METRA'. The serial number '44096 AX 144396 168' is visible at the bottom of the stamp.

(KELVIN FINSEN)

VALIDATION SHEET

Final Project Report

RISK MANAGEMENT STUDY IN CONSTRUCTION INDUSTRY IN YOGYAKARTA

By:

Kelvin Finsen

Student ID Number: 16 13 16354

Has been evaluated and approved by Supervisor Lecture

Yogyakarta, 4 April 2020

Supervisor,



(A. Koesmargono, Ir., MCM, Ph.D.)

Authorized by:

Civil Engineering Study Program




Head,

(AY. Harijanto Setiawan, Ir., M.Eng., Ph.D.)

EXAMINER VALIDATION SHEET

Final Project Report

RISK MANAGEMENT STUDY IN CONSTRUCTION INDUSTRY IN YOGYAKARTA

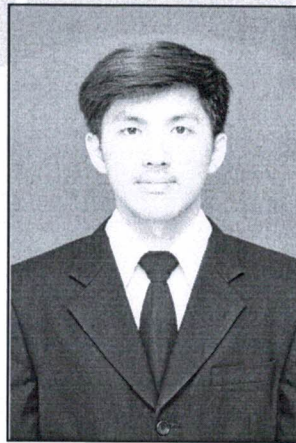




By:

Kelvin Finsen

Student ID Number: 16 13 16354

Has been evaluated and approved by:

	Name	Signature	Date
Head	: A. Koesmargono, Ir., MCM, Ph.D.	
Member	: Peter F. Kaming, Ir., M.Eng., Ph.D.	
Member	: Agustina Kiky A., S.T., M.Eng., Dr.Ing.	

PREFACE

Praise the presence of God Almighty for His gift and declaration so that the author can complete the final task titled Risk Management in Construction Industry in Yogyakarta.

In the process of preparing this final project, the author gathered a lot of help and assistance from various parties. Therefore, the author agrees to thanked:

1. Mr. Luky Handoko, S.T., M. Eng., Dr. Eng., as dean of the Faculty of Engineering of Atma Jaya University Yogyakarta.
2. Mr. Ir. Harijanto Setiawan, M. Eng., Ph.D., as the Head of the Atma Jaya Yogyakarta University Civil Engineering Study Program.
3. A. Koesmargono, Ir., MCM, Ph.D. as a Supervising Lecturer who has been willing and patient in guiding and giving so much help to the writer so that this Final Task can be completed well.
4. Mr. Dinar Gumilang Jati, S.T., M. Eng, as the final task coordinator.
5. All Lecturers of the Faculty of Engineering, Atma Jaya University, Yogyakarta, have been willing to educate, teach and share their knowledge with writers.
6. For parents, Mr. Harry Homer and Mrs. Stefanny Venezuela Pricillia and the families of Ellen Fredericia and Melissa Fredericia, who always provide encouragement, opportunity and always support in prayer and extraordinary affection.

7. Dear girlfriend Sally Wong for accompanying the writer during the completion of the thesis and always praying that the writer can finish the thesis quickly.
8. For my friends Ricky Martin, Kenneth, Edo, Thalia, Anita for supporting, joking and giving prayers from afar to the author.
9. For my beloved friends Benedict Angga, Fendy Heryanto, Fernando Situmeang, Felix Salvino, Willy Huang, Bertho, Peter Cantona, Felisitas Nindy, who have accompanied the writer for 4 years in Atma Jaya Yogyakarta.
10. For the Kamadhis Community who are close like family, they have given surprises to the writer and have opened the way for the writer to be active.
11. For ICEP big families because they have provided support and also provide answers very quickly when asked.
12. For TBB friends because they have given color to the author last year and have allowed the author to be a lab assistant.
13. And all the parties cannot be mentioned one.

At the end of the word, author realizes that the final task report is not yet perfect, so the authors need constructive criticism and advice and the author also hopes that this task is beneficial for everyone.

Yogyakarta, April 2020

Author

Kelvin Finsen.

NPM: 16 13 16354


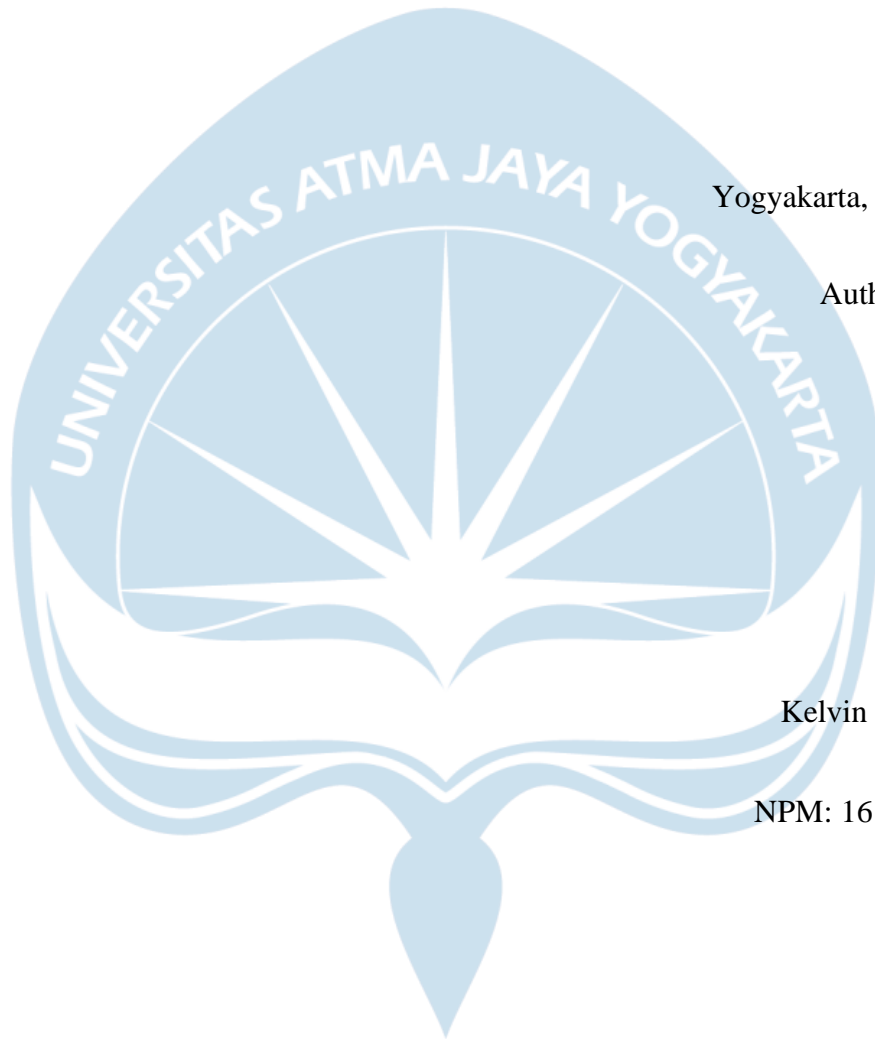


TABLE OF CONTENT

COVER	i
STATEMENT	ii
VALIDATION	iii
EXAMINER VALIDATION	iv
PREFACE	v
TABLE OF CONTENT	viii
LIST OF TABLE	xii
LIST OF FIGURE	xiv
ATTACHMENT	xv
BAB I INTRODUCTION	1
1.1 Background.....	1
1.2 Research Question	3
1.3 Scope and Limitation.....	3
1.4 Objectives and Benefits	4
1.5 Outline of the Thesis.....	4
1.6 Originality of the Thesis	5
BAB II LITERATURE RIVIEW	6
2.1 Project Definition	6
2.2 Construction Project	7
2.3 Project Management	8
2.4 Risk.....	9
2.5 Risk Management	12

2.6 Step in Risk Management.....	13
2.7 Risk Response.....	19
BAB III METHODOLOGY	21
3.1 Research Data	21
3.1.1 Type of Data.....	21
3.1.2 Target, Respopndent and Sample.....	21
3.2 How to Collect the Data	22
3.2.1 Literature Study.....	22
3.2.2 Observe Field Study.....	22
3.3 Data Analysis Method	22
3.3.1 Descpition Statistic	22
3.3.2 Calculating Mean	23
3.3.3 Calculating Standard Deviation	23
3.4 Questionnaire.....	24
3.5 Tools to Data Analysis	25
BAB IV DATA ANALYSIS AND DISCUSSION	26
4.1 General Data of Respondents	26
4.1.1 Classification of Respondents Based on Position	26
4.1.2 Classification of Respondents Based on Last Education	27
4.1.3 Classification of Respondents Based on Period.....	28
4.1.4 Classification of Respondents Based on Project Handled	29
4.2 Data Frequency Analysis.....	30
4.2.1 Risk Frequency Result for Each Risk Factor	30

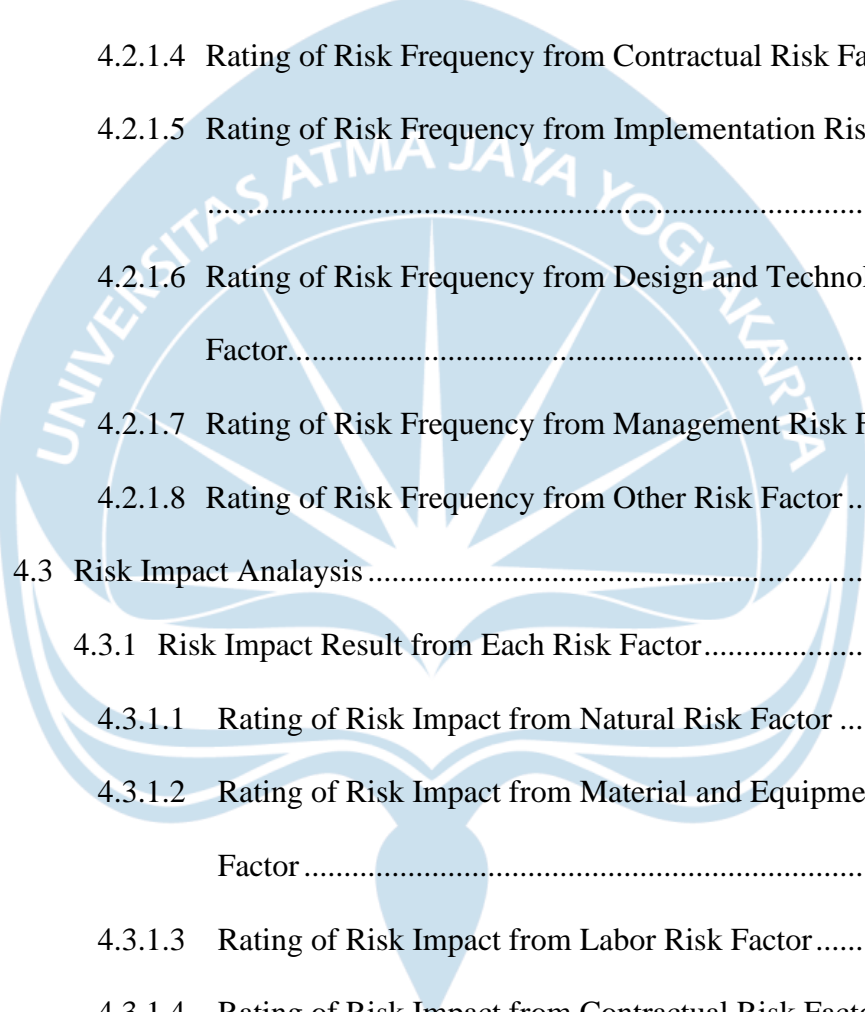


4.2.1.1	Rating of Risk Frequency from Natural Risk Factor	30
4.2.1.2	Rating of Risk Frequency from Material and Equipment Risk Factor.....	32
4.2.1.3	Rating of Risk Frequency from Labor Risk Factor.....	34
4.2.1.4	Rating of Risk Frequency from Contractual Risk Factor.....	35
4.2.1.5	Rating of Risk Frequency from Implementation Risk Factor	36
4.2.1.6	Rating of Risk Frequency from Design and Technology Risk Factor.....	38
4.2.1.7	Rating of Risk Frequency from Management Risk Factor ...	39
4.2.1.8	Rating of Risk Frequency from Other Risk Factor	41
4.3	Risk Impact Analysis	42
4.3.1	Risk Impact Result from Each Risk Factor.....	42
4.3.1.1	Rating of Risk Impact from Natural Risk Factor	43
4.3.1.2	Rating of Risk Impact from Material and Equipment Risk Factor	44
4.3.1.3	Rating of Risk Impact from Labor Risk Factor.....	46
4.3.1.4	Rating of Risk Impact from Contractual Risk Factor.....	47
4.3.1.5	Rating of Risk Impact from Implementation Risk Factor ...	48
4.3.1.6	Rating of Risk Impact from Design and Technology Risk Factor	49

4.3.1.7	Rating of Risk Impact from Management Risk Factor.....	51
4.3.1.8	Rating of Risk Impact from Other Risk Factor	52
4.4	Risk Response.....	53
4.4.1	Risk Response from Natural Risk Factor.....	53
4.4.2	Risk Response from Material and Equipment Risk Factor.....	55
4.4.3	Risk Response from Labor Risk Factor	58
4.4.4	Risk Response from Contractual Risk Factor	60
4.4.5	Risk Response from Implementation Risk Factor	63
4.4.6	Risk Response from Design and Technology Risk Factor.....	69
4.4.7	Risk Response from Management Risk Factor.....	72
4.4.8	Risk Response from Other Risk Factor.....	76
BAB V	CONCLUSION AND RECOMMENDATION.....	78
5.1	Background.....	78
5.2	Suggestion	79
REFERENCE.....		80
ATTCHMENT		82

LIST OF TABEL


Tabel 2.1 Risk/Work Breakdown Structure	14
Tabel 2.2 Five Point Scale Work for Project	16
Tabel 2.3 Input of Risk Monitoring and Control	18
Tabel 3.1 Likert Scale	24
Tabel 4.1 Classification of Respondents Based on Position.....	27
Tabel 4.2 Classification of Respondents Based on Last Education.....	27
Tabel 4.3 Classification of Respondents Based on Period Working	28
Tabel 4.4 Classification of Respondents Based on Project Being Handled.....	29
Tabel 4.5 Rating of Risk Frequency from Natural Risk Factors.....	31
Tabel 4.6 Rating of Risk Frequency from Material and Equipment Risk Factors.....	33
Tabel 4.7 Rating of Risk Frequency from Labor Risk Factors	34
Tabel 4.8 Rating of Risk Frequency from Contractual Risk Factors.....	35
Tabel 4.9 Rating of Risk Frequency from Implementation Risk Factors	37
Tabel 4.10 Rating of Risk Frequency from Design and Technology Risk Factors	39
Tabel 4.11 Rating of Risk Frequency from Management Risk Factors.....	40
Tabel 4.12 Rating of Risk Frequency from Other Risk Factors	42
Tabel 4.13 Rating of Risk Impact from Natural Risk Factors	44
Tabel 4.14 Rating of Risk Impact from Material and Equipment Risk Factors	45
Tabel 4.15 Rating of Risk Impact from Labor Risk Factors.....	46
Tabel 4.16 Rating of Risk Impact from Contractual Risk Factors.....	47
Tabel 4.17 Rating of Risk Impact from Implementation Risk Factors	48
Tabel 4.18 Rating of Risk Impact from Design and Technology Risk Factors	50

Tabel 4.19 Rating of Risk Impact from Management Risk Factors	51
Tabel 4.20 Rating of Risk Impact from Other Risk Factors	52
Tabel 4.21 Risk Response from Natural Risk Factors	53
Tabel 4.22 Risk Response from Material and Equipment Risk Factors	55
Tabel 4.23 Risk Response from Labor Risk Factors.....	58
Tabel 4.24 Risk Response from Contractual Risk Factors	61
Tabel 4.25 Risk Response from Implementation Risk Factors.....	63
Tabel 4.26 Risk Response from Design and Technology Risk Factors.....	69
Tabel 4.27 Risk Response from Management Risk Factors	72
Tabel 4.28 Risk Response from Other Risk Factors	76



LIST OF FIGURES

Figure 2.1 Project Life Cycle	10
Figure 2.2 Hierarchy of Risk at Building Project in Indonesia.....	11
Figure 2.3 Five Basic Ways Through Which Risk Identification is Done.....	15



LIST OF ATTACHMENT

Attachment 1. Questionnaire Distribution Permission/Approval

Attachment 2. Research Questionnaire

Attachment 3. Table of Project Name

